





ID	Unavail	FX Roll	Publish	FX Project	Task Name	% Complete	Duration	Work	Baseline Start	Baseline Finish	Start	Finish	Finish Variance	Predecessor	Successor	FX Task Role	Resource Names	Jun 30, '19	Jul 7, '19	Jul 14, '19
																		S	S	S
0					TEMPLATE: DDI Project Schedule	0%	585 days	0 hrs	NA	NA	Mon 7/1/19	Wed 12/1/21	0 days							
1					TEMPLATE: DDI Project Schedule	0%	585 days	0 hrs	NA	NA	Mon 7/1/19	Wed 12/1/21	0 days							
2					Project Start	0%	0 days	0 hrs	NA	NA	Mon 7/1/19	Mon 7/1/19	0 days							
3					Project Authorization	0%	0 days	0 hrs	NA	NA	Mon 7/1/19	Mon 7/1/19	0 days		5,8,11,17					
4					Project Management	0%	569 days	0 hrs	NA	NA	Mon 7/1/19	Mon 11/1/21	0 days							
5					Manage Project (includes maintain schedule, CRAIDL, artifact)	0%	569 days	0 hrs	NA	NA	Mon 7/1/19	Mon 11/1/21	0 days	3	385					
6					Initiation	0%	15 days	0 hrs	NA	NA	Mon 7/1/19	Mon 7/22/19	0 days							
7					DMS Risk and Complexity Assessment Pre-Charter	0%	2 days	0 hrs	NA	NA	Mon 7/1/19	Tue 7/2/19	0 days							
8					Complete DMS Risk and Complexity Assessment (R&C) Pre	0%	1 day	0 hrs	NA	NA	Mon 7/1/19	Mon 7/1/19	0 days	3	9					
9					Review DMS Risk and Complexity Assessment (R&C) by FX	0%	1 day	0 hrs	NA	NA	Tue 7/2/19	Tue 7/2/19	0 days	8	14					
10					Project Process Agreement (PPA)	0%	2 days	0 hrs	NA	NA	Mon 7/1/19	Tue 7/2/19	0 days							
11					Complete Project Process Agreement (PPA) (includes agre	0%	1 day	0 hrs	NA	NA	Mon 7/1/19	Mon 7/1/19	0 days	3	12					
12					Review Project Process Agreement (PPA) by FX EPMO	0%	1 day	0 hrs	NA	NA	Tue 7/2/19	Tue 7/2/19	0 days	11	13					
13					Review Project Process Agreement (PPA) and R&C Assesse	0%	1 day	0 hrs	NA	NA	Wed 7/3/19	Wed 7/3/19	0 days	12	14					
14					Conducts New Project Orientation (EPMO)	0%	1 day	0 hrs	NA	NA	Fri 7/5/19	Fri 7/5/19	0 days	13	15					
15					Establishes Infrastructure for New Project (EPMO)	0%	1 day	0 hrs	NA	NA	Mon 7/8/19	Mon 7/8/19	0 days	14	17FF					
16					Project Charter	0%	13 days	0 hrs	NA	NA	Mon 7/1/19	Thu 7/18/19	0 days							
17					Draft Project Charter	0%	5 days	0 hrs	NA	NA	Mon 7/1/19	Mon 7/8/19	0 days	3,15FF	18					
18					Review Draft Project Charter by FX EPMO	0%	1 day	0 hrs	NA	NA	Tue 7/9/19	Tue 7/9/19	0 days	17	19SS					
19					Update Draft Project Charter Based on FX EPMO Review	0%	1 day	0 hrs	NA	NA	Tue 7/9/19	Tue 7/9/19	0 days	18SS	20					
20					Review Draft Project Charter by SEAS	0%	1 day	0 hrs	NA	NA	Wed 7/10/19	Wed 7/10/19	0 days	19	21SS					
21					Update Draft Project Charter Based Upon SEAS Review	0%	1 day	0 hrs	NA	NA	Wed 7/10/19	Wed 7/10/19	0 days	20SS	22					
22					Walk Through Project Charter with AHCA	0%	1 day	0 hrs	NA	NA	Thu 7/11/19	Thu 7/11/19	0 days	21	23FF					
23					Update Charter Based Upon AHCA Review Comments	0%	1 day	0 hrs	NA	NA	Thu 7/11/19	Thu 7/11/19	0 days	22FF	24					
24					QC Review of Draft Project Charter	0%	1 day	0 hrs	NA	NA	Fri 7/12/19	Fri 7/12/19	0 days	23	25FF					
25					Update Draft Project Charter Based Upon QC Review	0%	1 day	0 hrs	NA	NA	Fri 7/12/19	Fri 7/12/19	0 days	24FF	26FF					
26					Submit Project Charter for Governance Review	0%	1 day	0 hrs	NA	NA	Fri 7/12/19	Fri 7/12/19	0 days	25FF	28,37,52					
27					Governance Review	0%	4 days	0 hrs	NA	NA	Mon 7/15/19	Thu 7/18/19	0 days							
28					Review Project Charter and Assigns Project Sponsor (Gc	0%	4 days	0 hrs	NA	NA	Mon 7/15/19	Thu 7/18/19	0 days	26	29FF					
29					Recommends Approval of Project Charter (Governance	0%	1 day	0 hrs	NA	NA	Thu 7/18/19	Thu 7/18/19	0 days	28FF	30					
30					Project Charter Complete	0%	0 days	0 hrs	NA	NA	Thu 7/18/19	Thu 7/18/19	0 days	29	31,34					
31					Complete DMS Initiation Gate R&C	0%	1 day	0 hrs	NA	NA	Fri 7/19/19	Fri 7/19/19	0 days	30	34,32,33					
32					Review and Updated existing OCM Artifacts and Tools	0%	1 day	0 hrs	NA	NA	Mon 7/22/19	Mon 7/22/19	0 days	31	34					
33					Conduct FX Compliance Assessment Review	0%	1 day	0 hrs	NA	NA	Mon 7/22/19	Mon 7/22/19	0 days	31	34					
34					Initiation Phase Complete	0%	0 days	0 hrs	NA	NA	Mon 7/22/19	Mon 7/22/19	0 days	30,31,32,38						
35					Planning	0%	71 days	0 hrs	NA	NA	Mon 7/15/19	Tue 10/22/19	0 days							
36					Project Management Plan (per O-2, P-2, P-3 Standards)	0%	16 days	0 hrs	NA	NA	Mon 7/15/19	Mon 8/5/19	0 days							
37					Complete Project Management Plan (PMP)	0%	5 days	0 hrs	NA	NA	Mon 7/15/19	Fri 7/19/19	0 days	26	38					
38					Review Draft Project Management Plan (PMP) by FX EPM	0%	1 day	0 hrs	NA	NA	Tue 7/23/19	Tue 7/23/19	0 days	37,34	39FF					
39					Update Draft Project Management Plan (PMP)	0%	1 day	0 hrs	NA	NA	Tue 7/23/19	Tue 7/23/19	0 days	38FF	40					
40					Walk Through Project Management Plan with AHCA	0%	1 day	0 hrs	NA	NA	Wed 7/24/19	Wed 7/24/19	0 days	39	41FF					
41					Update Project Management Plan Based on AHCA Review	0%	1 day	0 hrs	NA	NA	Wed 7/24/19	Wed 7/24/19	0 days	40FF	42					
42					QC Review of Draft Project Management Plan	0%	2 days	0 hrs	NA	NA	Thu 7/25/19	Fri 7/26/19	0 days	41	43					
43					Update Draft Project Management Plan on QC Review	0%	1 day	0 hrs	NA	NA	Mon 7/29/19	Mon 7/29/19	0 days	42	44SS					
44					Submit Draft Project Management Plan to AHCA	0%	1 day	0 hrs	NA	NA	Mon 7/29/19	Mon 7/29/19	0 days	43SS	45SS					
45					AHCA Reviews Draft Project Management Plan	0%	5 days	0 hrs	NA	NA	Mon 7/29/19	Fri 8/2/19	0 days	44SS	46					
46					Update Draft Project Management Plan Based upon AHCA	0%	1 day	0 hrs	NA	NA	Mon 8/5/19	Mon 8/5/19	0 days	45	47					
47					AHCA Approves Project Management Plan	0%	0 days	0 hrs	NA	NA	Mon 8/5/19	Mon 8/5/19	0 days	46	118,131,					
48					Process Inventory	0%	6 days	0 hrs	NA	NA	Mon 7/15/19	Mon 7/22/19	0 days							
49					Prepare Process Inventory	0%	5 days	0 hrs	NA	NA	Mon 7/15/19	Fri 7/19/19	0 days	26	50					
50					Validate Process Inventory with AHCA	0%	1 day	0 hrs	NA	NA	Mon 7/22/19	Mon 7/22/19	0 days	49	140,58,1					
51					Work Breakdown Structure (WBS)	0%	5 days	0 hrs	NA	NA	Wed 7/17/19	Tue 7/23/19	0 days							
52					Conduct Workshop 1 - WBS Levels 1, 2, 3	0%	1 day	0 hrs	NA	NA	Wed 7/17/19	Wed 7/17/19	0 days	26FS+2	d53					
53					Conduct Workshop 2 - WBS Level 4	0%	1 day	0 hrs	NA	NA	Thu 7/18/19	Thu 7/18/19	0 days	52	54					
54					Conduct Workshop 3 - WBS Level 5 and Task Sequencing	0%	1 day	0 hrs	NA	NA	Fri 7/19/19	Fri 7/19/19	0 days	53	55					
55					Conduct Workshop 4 - Resources and Availability	0%	1 day	0 hrs	NA	NA	Mon 7/22/19	Mon 7/22/19	0 days	54	56					
56					Conduct Workshop 5 - Estimate Level of Effort and Durati	0%	1 day	0 hrs	NA	NA	Tue 7/23/19	Tue 7/23/19	0 days	55	58,118					
57					Project Schedule	0%	20 days	0 hrs	NA	NA	Wed 7/24/19	Tue 8/20/19	0 days							
58					Create Draft Project Schedule (include all artifacts identi	0%	10 days	0 hrs	NA	NA	Wed 7/24/19	Tue 8/6/19	0 days	56,50	59					
59					QC of Draft Project Schedule	0%	1 day	0 hrs	NA	NA	Wed 8/7/19	Wed 8/7/19	0 days	58	60					
60					Update Draft Project Schedule Upon QC Review	0%	1 day	0 hrs	NA	NA	Thu 8/8/19	Thu 8/8/19	0 days	59	61					
61					Walk Through Project Schedule with AHCA	0%	1 day	0 hrs	NA	NA	Fri 8/9/19	Fri 8/9/19	0 days	60	62					
62					Update Project Schedule Based Upon AHCA Review Comrn	0%	1 day	0 hrs	NA	NA	Mon 8/12/19	Mon 8/12/19	0 days	61	63					
63					Submit Project Schedule to AHCA	0%	1 day	0 hrs	NA	NA	Tue 8/13/19	Tue 8/13/19	0 days	62	64					



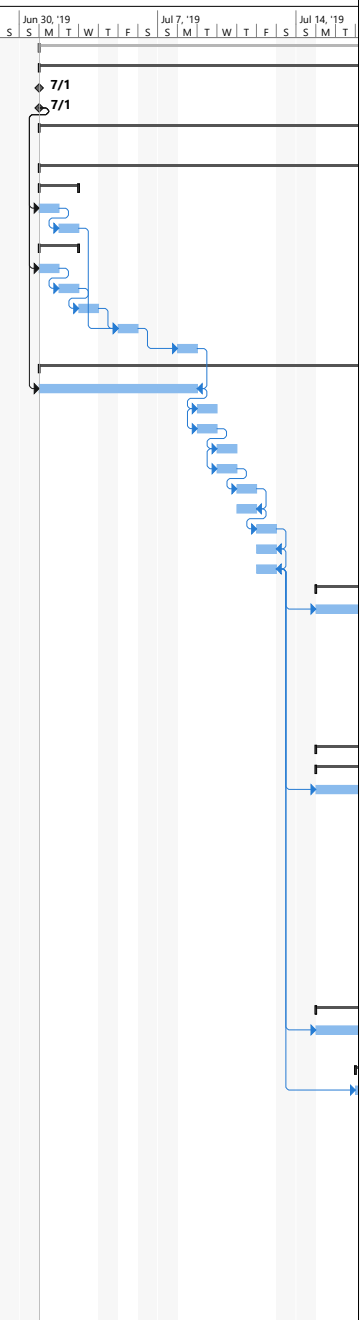

W T F S | Jul 21, '19 | Jul 28, '19 | Aug 4, '19 | Aug 11, '19 | Aug 18, '19 | Aug 25, '19 | Sep 1, '19 | Sep 8, '19 | Sep 15, '19 | Sep 22, '19 | Sep 29, '19 | Oct 6, '19 | Oct 13, '19 | Oct 20, '19

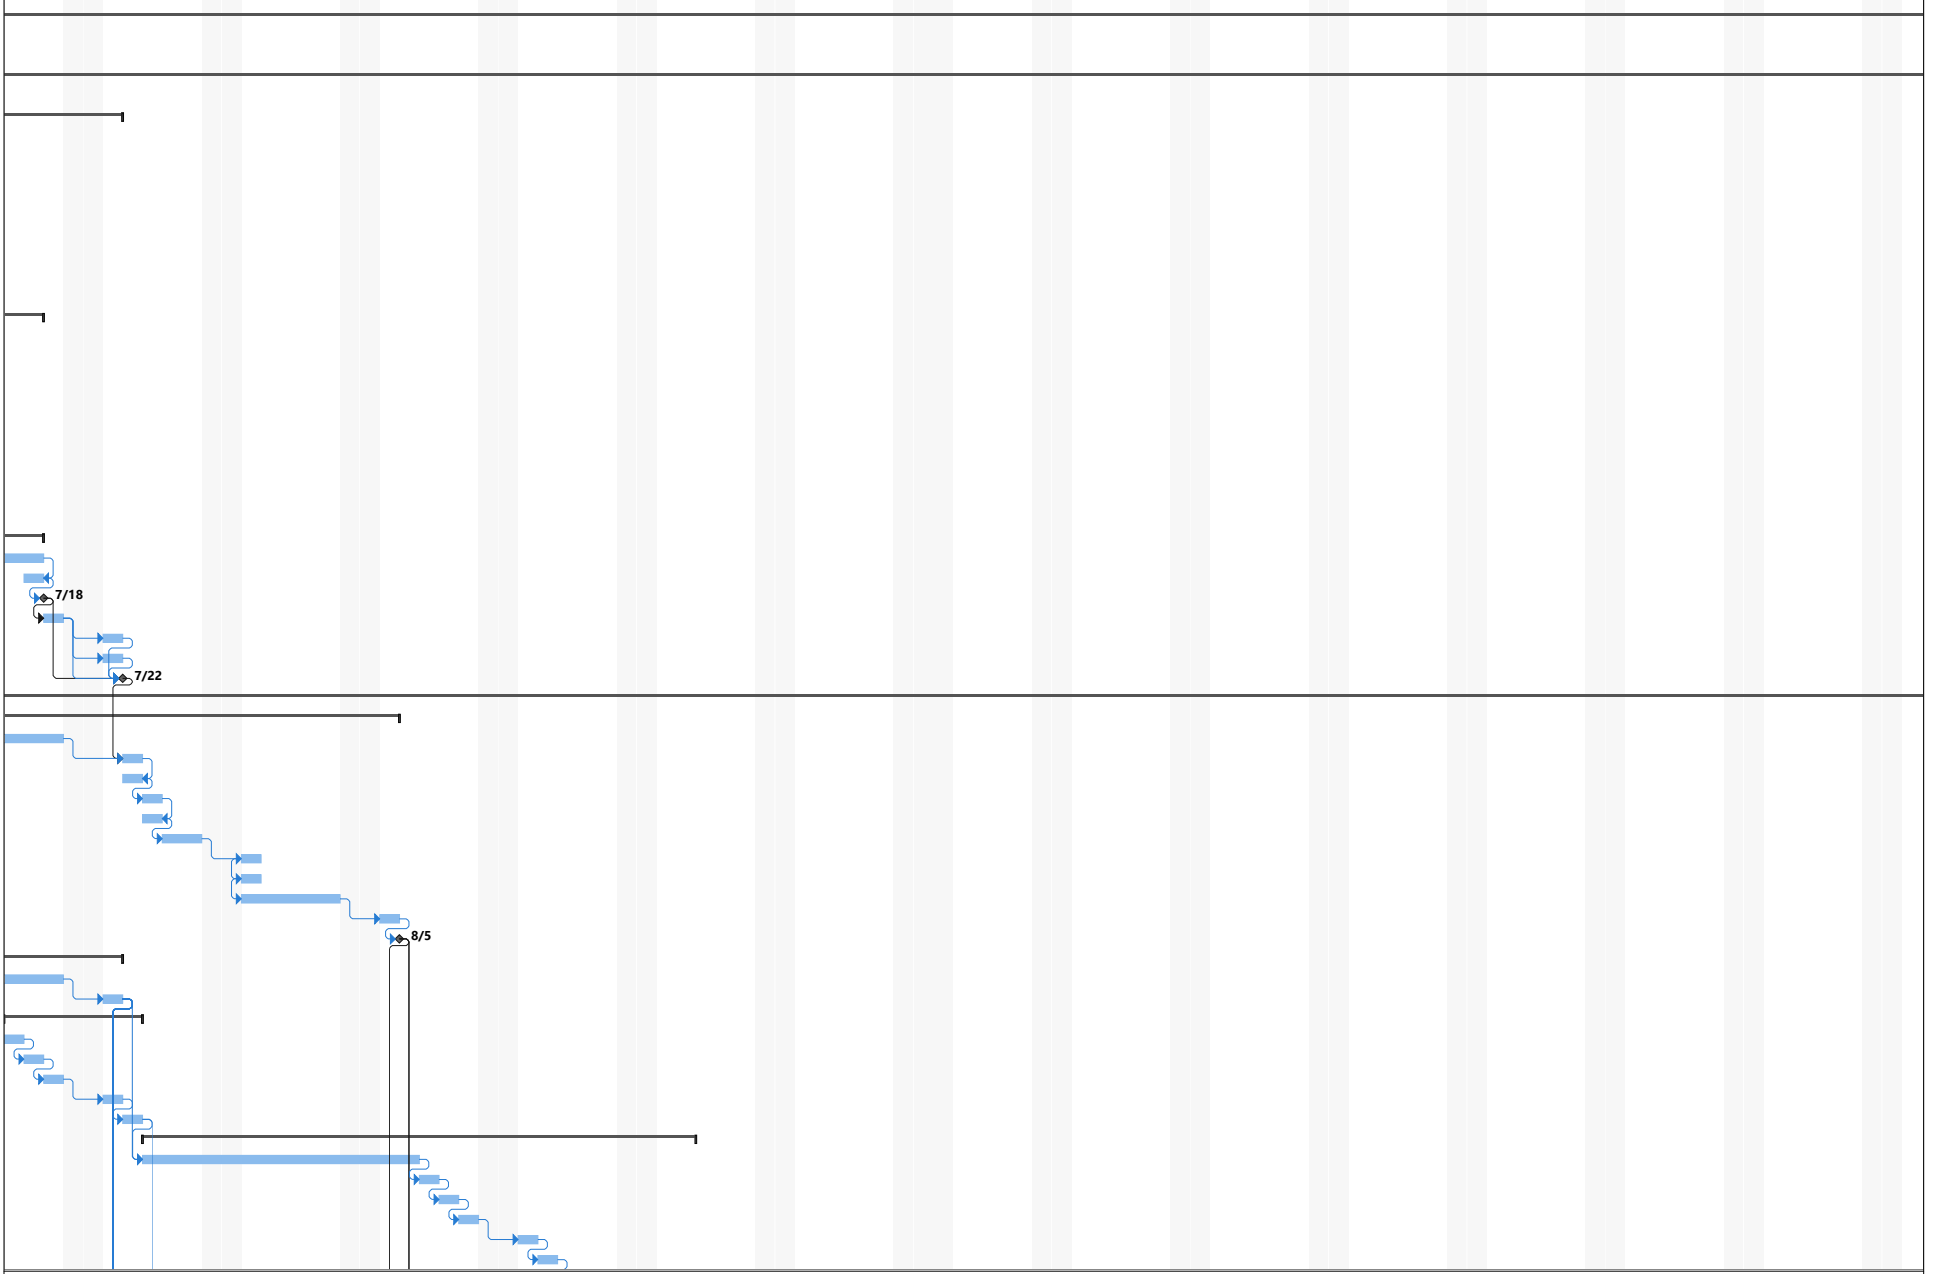



W	T	F	S	Jul 21, '19	S	M	T	W	T	F	S	Jul 28, '19	S	M	T	W	T	F	S	Aug 4, '19	S	M	T	W	T	F	S	Aug 11, '19	S	M	T	W	T	F	S	Aug 18, '19	S	M	T	W	T	F	S	Aug 25, '19	S	M	T	W	T	F	S	Sep 1, '19	S	M	T	W	T	F	S	Sep 8, '19	S	M	T	W	T	F	S	Sep 15, '19	S	M	T	W	T	F	S	Sep 22, '19	S	M	T	W	T	F	S	Sep 29, '19	S	M	T	W	T	F	S	Oct 6, '19	S	M	T	W	T	F	S	Oct 13, '19	S	M	T	W	T	F	S	Oct 20, '19	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---



W	T	F	S	Jul 21, '19	S	M	T	W	T	F	S	Jul 28, '19	S	M	T	W	T	F	S	Aug 4, '19	S	M	T	W	T	F	S	Aug 11, '19	S	M	T	W	T	F	S	Aug 18, '19	S	M	T	W	T	F	S	Aug 25, '19	S	M	T	W	T	F	S	Sep 1, '19	S	M	T	W	T	F	S	Sep 8, '19	S	M	T	W	T	F	S	Sep 15, '19	S	M	T	W	T	F	S	Sep 22, '19	S	M	T	W	T	F	S	Sep 29, '19	S	M	T	W	T	F	S	Oct 6, '19	S	M	T	W	T	F	S	Oct 13, '19	S	M	T	W	T	F	S	Oct 20, '19	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---



W	T	F	S	Jul 21, '19	S	M	T	W	T	F	S	Jul 28, '19	S	M	T	W	T	F	S	Aug 4, '19	S	M	T	W	T	F	S	Aug 11, '19	S	M	T	W	T	F	S	Aug 18, '19	S	M	T	W	T	F	S	Aug 25, '19	S	M	T	W	T	F	S	Sep 1, '19	S	M	T	W	T	F	S	Sep 8, '19	S	M	T	W	T	F	S	Sep 15, '19	S	M	T	W	T	F	S	Sep 22, '19	S	M	T	W	T	F	S	Sep 29, '19	S	M	T	W	T	F	S	Oct 6, '19	S	M	T	W	T	F	S	Oct 13, '19	S	M	T	W	T	F	S	Oct 20, '19	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---



19	Oct 27, '19	Nov 3, '19	Nov 10, '19	Nov 17, '19	Nov 24, '19	Dec 1, '19	Dec 8, '19	Dec 15, '19	Dec 22, '19	Dec 29, '19	Jan 5, '20	Jan 12, '20	Jan 19, '20	Jan
T	S	S	S	S	S	S	S	S	S	S	S	S	S	S
W	M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F	F
S	S	S	S	S	S	S	S	S	S	S	S	S	S	S



26, '20	Feb 2, '20	Feb 9, '20	Feb 16, '20	Feb 23, '20	Mar 1, '20	Mar 8, '20	Mar 15, '20	Mar 22, '20	Mar 29, '20	Apr 5, '20	Apr 12, '20	Apr 19, '20	Apr 26, '20
M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S

--	--	--	--	--	--	--	--	--	--	--	--	--	--

--	--	--	--	--	--	--	--	--	--	--	--	--	--

--	--	--	--	--	--	--	--	--	--	--	--	--	--



26, '20	Feb 2, '20	Feb 9, '20	Feb 16, '20	Feb 23, '20	Mar 1, '20	Mar 8, '20	Mar 15, '20	Mar 22, '20	Mar 29, '20	Apr 5, '20	Apr 12, '20	Apr 19, '20	Apr 26, '20
M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S


[Empty grid area for data entry]													
----------------------------------	--	--	--	--	--	--	--	--	--	--	--	--	--



May 3, '20	May 10, '20	May 17, '20	May 24, '20	May 31, '20	Jun 7, '20	Jun 14, '20	Jun 21, '20	Jun 28, '20	Jul 5, '20	Jul 12, '20	Jul 19, '20	Jul 26, '20	Aug 2, '20
S	S	S	S	S	S	S	S	S	S	S	S	S	S
M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T
W	W	W	W	W	W	W	W	W	W	W	W	W	W
T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F



May 3, '20 May 10, '20 May 17, '20 May 24, '20 May 31, '20 Jun 7, '20 Jun 14, '20 Jun 21, '20 Jun 28, '20 Jul 5, '20 Jul 12, '20 Jul 19, '20 Jul 26, '20 Aug 2, '20
S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S

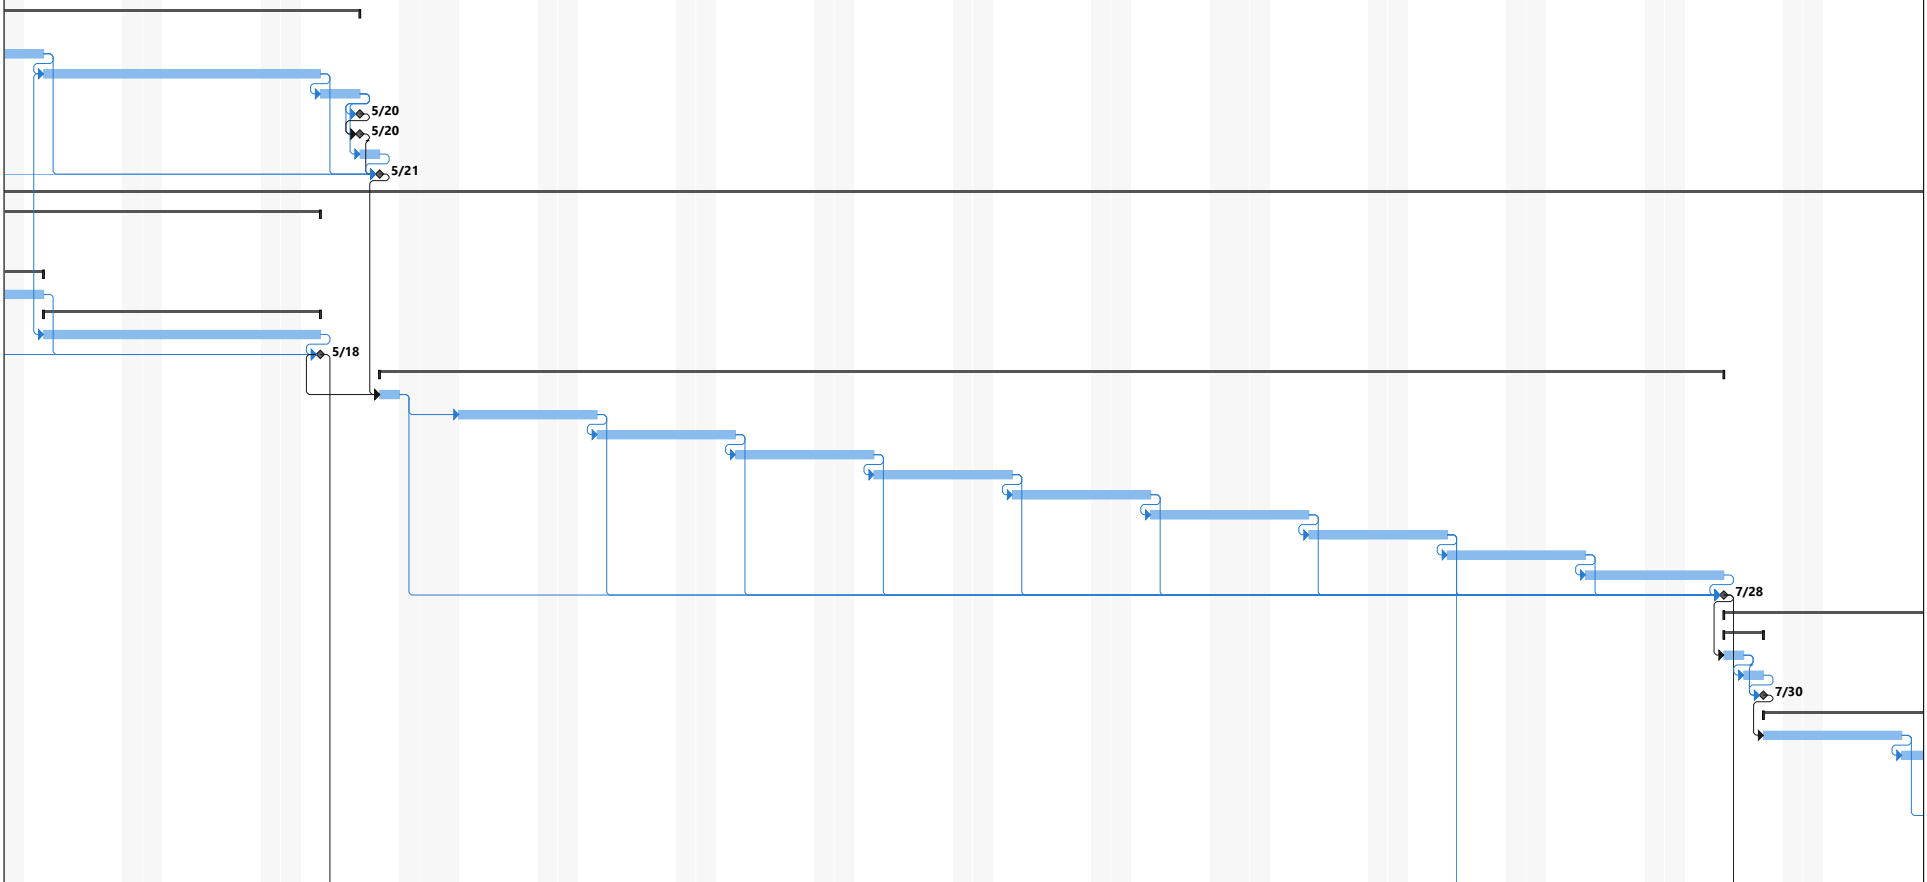



May 3, '20	May 10, '20	May 17, '20	May 24, '20	May 31, '20	Jun 7, '20	Jun 14, '20	Jun 21, '20	Jun 28, '20	Jul 5, '20	Jul 12, '20	Jul 19, '20	Jul 26, '20	Aug 2, '20
S	S	S	S	S	S	S	S	S	S	S	S	S	S
M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T
W	W	W	W	W	W	W	W	W	W	W	W	W	W
T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F



May 3, '20	May 10, '20	May 17, '20	May 24, '20	May 31, '20	Jun 7, '20	Jun 14, '20	Jun 21, '20	Jun 28, '20	Jul 5, '20	Jul 12, '20	Jul 19, '20	Jul 26, '20	Aug 2, '20
S	S	S	S	S	S	S	S	S	S	S	S	S	S
M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T
W	W	W	W	W	W	W	W	W	W	W	W	W	W
T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F



May 3, '20	May 10, '20	May 17, '20	May 24, '20	May 31, '20	Jun 7, '20	Jun 14, '20	Jun 21, '20	Jun 28, '20	Jul 5, '20	Jul 12, '20	Jul 19, '20	Jul 26, '20	Aug 2, '20
S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S


[Empty grid area for data entry]													
----------------------------------	--	--	--	--	--	--	--	--	--	--	--	--	--



Aug 9, '20	Aug 16, '20	Aug 23, '20	Aug 30, '20	Sep 6, '20	Sep 13, '20	Sep 20, '20	Sep 27, '20	Oct 4, '20	Oct 11, '20	Oct 18, '20	Oct 25, '20	Nov 1, '20	Nov 8, '20
S	S	S	S	S	S	S	S	S	S	S	S	S	S
M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T
W	W	W	W	W	W	W	W	W	W	W	W	W	W
T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F
S	S	S	S	S	S	S	S	S	S	S	S	S	S



Aug 9, '20	Aug 16, '20	Aug 23, '20	Aug 30, '20	Sep 6, '20	Sep 13, '20	Sep 20, '20	Sep 27, '20	Oct 4, '20	Oct 11, '20	Oct 18, '20	Oct 25, '20	Nov 1, '20	Nov 8, '20
S	S	S	S	S	S	S	S	S	S	S	S	S	S
M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T
W	W	W	W	W	W	W	W	W	W	W	W	W	W
T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F
S	S	S	S	S	S	S	S	S	S	S	S	S	S

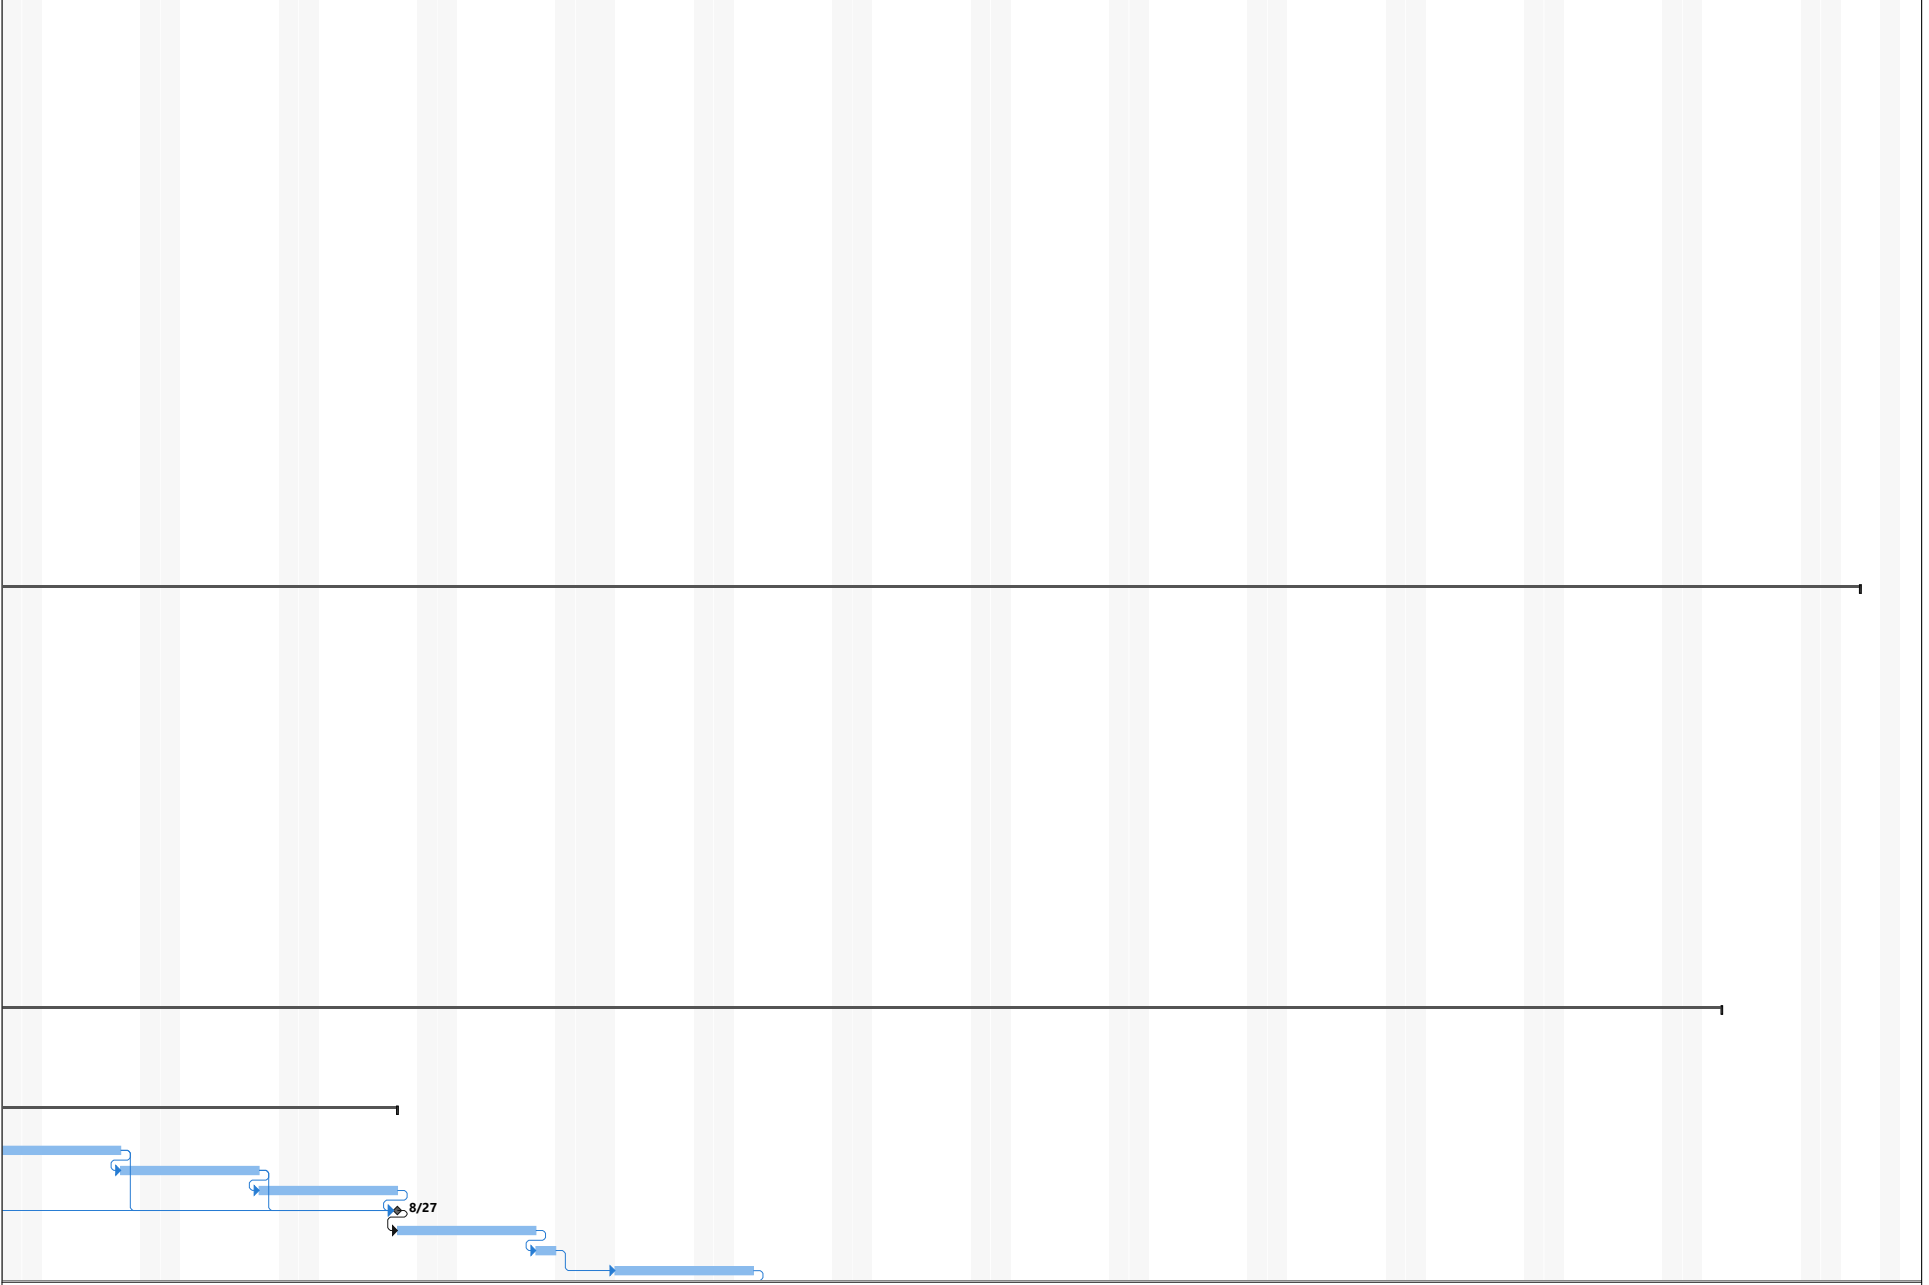



Aug 9, '20	Aug 16, '20	Aug 23, '20	Aug 30, '20	Sep 6, '20	Sep 13, '20	Sep 20, '20	Sep 27, '20	Oct 4, '20	Oct 11, '20	Oct 18, '20	Oct 25, '20	Nov 1, '20	Nov 8, '20
S	S	S	S	S	S	S	S	S	S	S	S	S	S
M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T
W	W	W	W	W	W	W	W	W	W	W	W	W	W
T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F
S	S	S	S	S	S	S	S	S	S	S	S	S	S



Aug 9, '20	Aug 16, '20	Aug 23, '20	Aug 30, '20	Sep 6, '20	Sep 13, '20	Sep 20, '20	Sep 27, '20	Oct 4, '20	Oct 11, '20	Oct 18, '20	Oct 25, '20	Nov 1, '20	Nov 8, '20
S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S

[Empty grid area for data entry]													
----------------------------------	--	--	--	--	--	--	--	--	--	--	--	--	--



W	T	F	S	May 30, '21	S	M	T	W	T	F	S	Jun 6, '21	S	M	T	W	T	F	S	Jun 13, '21	S	M	T	W	T	F	S	Jun 20, '21	S	M	T	W	T	F	S	Jun 27, '21	S	M	T	W	T	F	S	Jul 4, '21	S	M	T	W	T	F	S	Jul 11, '21	S	M	T	W	T	F	S	Jul 18, '21	S	M	T	W	T	F	S	Jul 25, '21	S	M	T	W	T	F	S	Aug 1, '21	S	M	T	W	T	F	S	Aug 8, '21	S	M	T	W	T	F	S	Aug 15, '21	S	M	T	W	T	F	S	Aug 22, '21	S	M	T	W	T	F	S	Aug 29, '21	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---



W	T	F	S	May 30, '21	S	M	T	W	T	F	S	Jun 6, '21	S	M	T	W	T	F	S	Jun 13, '21	S	M	T	W	T	F	S	Jun 20, '21	S	M	T	W	T	F	S	Jun 27, '21	S	M	T	W	T	F	S	Jul 4, '21	S	M	T	W	T	F	S	Jul 11, '21	S	M	T	W	T	F	S	Jul 18, '21	S	M	T	W	T	F	S	Jul 25, '21	S	M	T	W	T	F	S	Aug 1, '21	S	M	T	W	T	F	S	Aug 8, '21	S	M	T	W	T	F	S	Aug 15, '21	S	M	T	W	T	F	S	Aug 22, '21	S	M	T	W	T	F	S	Aug 29, '21	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---



W	T	F	S	May 30, '21	S	M	T	W	T	F	S	Jun 6, '21	S	M	T	W	T	F	S	Jun 13, '21	S	M	T	W	T	F	S	Jun 20, '21	S	M	T	W	T	F	S	Jun 27, '21	S	M	T	W	T	F	S	Jul 4, '21	S	M	T	W	T	F	S	Jul 11, '21	S	M	T	W	T	F	S	Jul 18, '21	S	M	T	W	T	F	S	Jul 25, '21	S	M	T	W	T	F	S	Aug 1, '21	S	M	T	W	T	F	S	Aug 8, '21	S	M	T	W	T	F	S	Aug 15, '21	S	M	T	W	T	F	S	Aug 22, '21	S	M	T	W	T	F	S	Aug 29, '21	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---




W	T	F	S	May 30, '21	S	M	T	W	T	F	S	Jun 6, '21	S	M	T	W	T	F	S	Jun 13, '21	S	M	T	W	T	F	S	Jun 20, '21	S	M	T	W	T	F	S	Jun 27, '21	S	M	T	W	T	F	S	Jul 4, '21	S	M	T	W	T	F	S	Jul 11, '21	S	M	T	W	T	F	S	Jul 18, '21	S	M	T	W	T	F	S	Jul 25, '21	S	M	T	W	T	F	S	Aug 1, '21	S	M	T	W	T	F	S	Aug 8, '21	S	M	T	W	T	F	S	Aug 15, '21	S	M	T	W	T	F	S	Aug 22, '21	S	M	T	W	T	F	S	Aug 29, '21	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---



W	T	F	S	May 30, '21	S	M	T	W	T	F	S	Jun 6, '21	S	M	T	W	T	F	S	Jun 13, '21	S	M	T	W	T	F	S	Jun 20, '21	S	M	T	W	T	F	S	Jun 27, '21	S	M	T	W	T	F	S	Jul 4, '21	S	M	T	W	T	F	S	Jul 11, '21	S	M	T	W	T	F	S	Jul 18, '21	S	M	T	W	T	F	S	Jul 25, '21	S	M	T	W	T	F	S	Aug 1, '21	S	M	T	W	T	F	S	Aug 8, '21	S	M	T	W	T	F	S	Aug 15, '21	S	M	T	W	T	F	S	Aug 22, '21	S	M	T	W	T	F	S	Aug 29, '21	S	M
---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---



21 | Sep 5, '21 | Sep 12, '21 | Sep 19, '21 | Sep 26, '21 | Oct 3, '21 | Oct 10, '21 | Oct 17, '21 | Oct 24, '21 | Oct 31, '21 | Nov 7, '21 | Nov 14, '21 | Nov 21, '21 | Nov 28, '21 | Dec

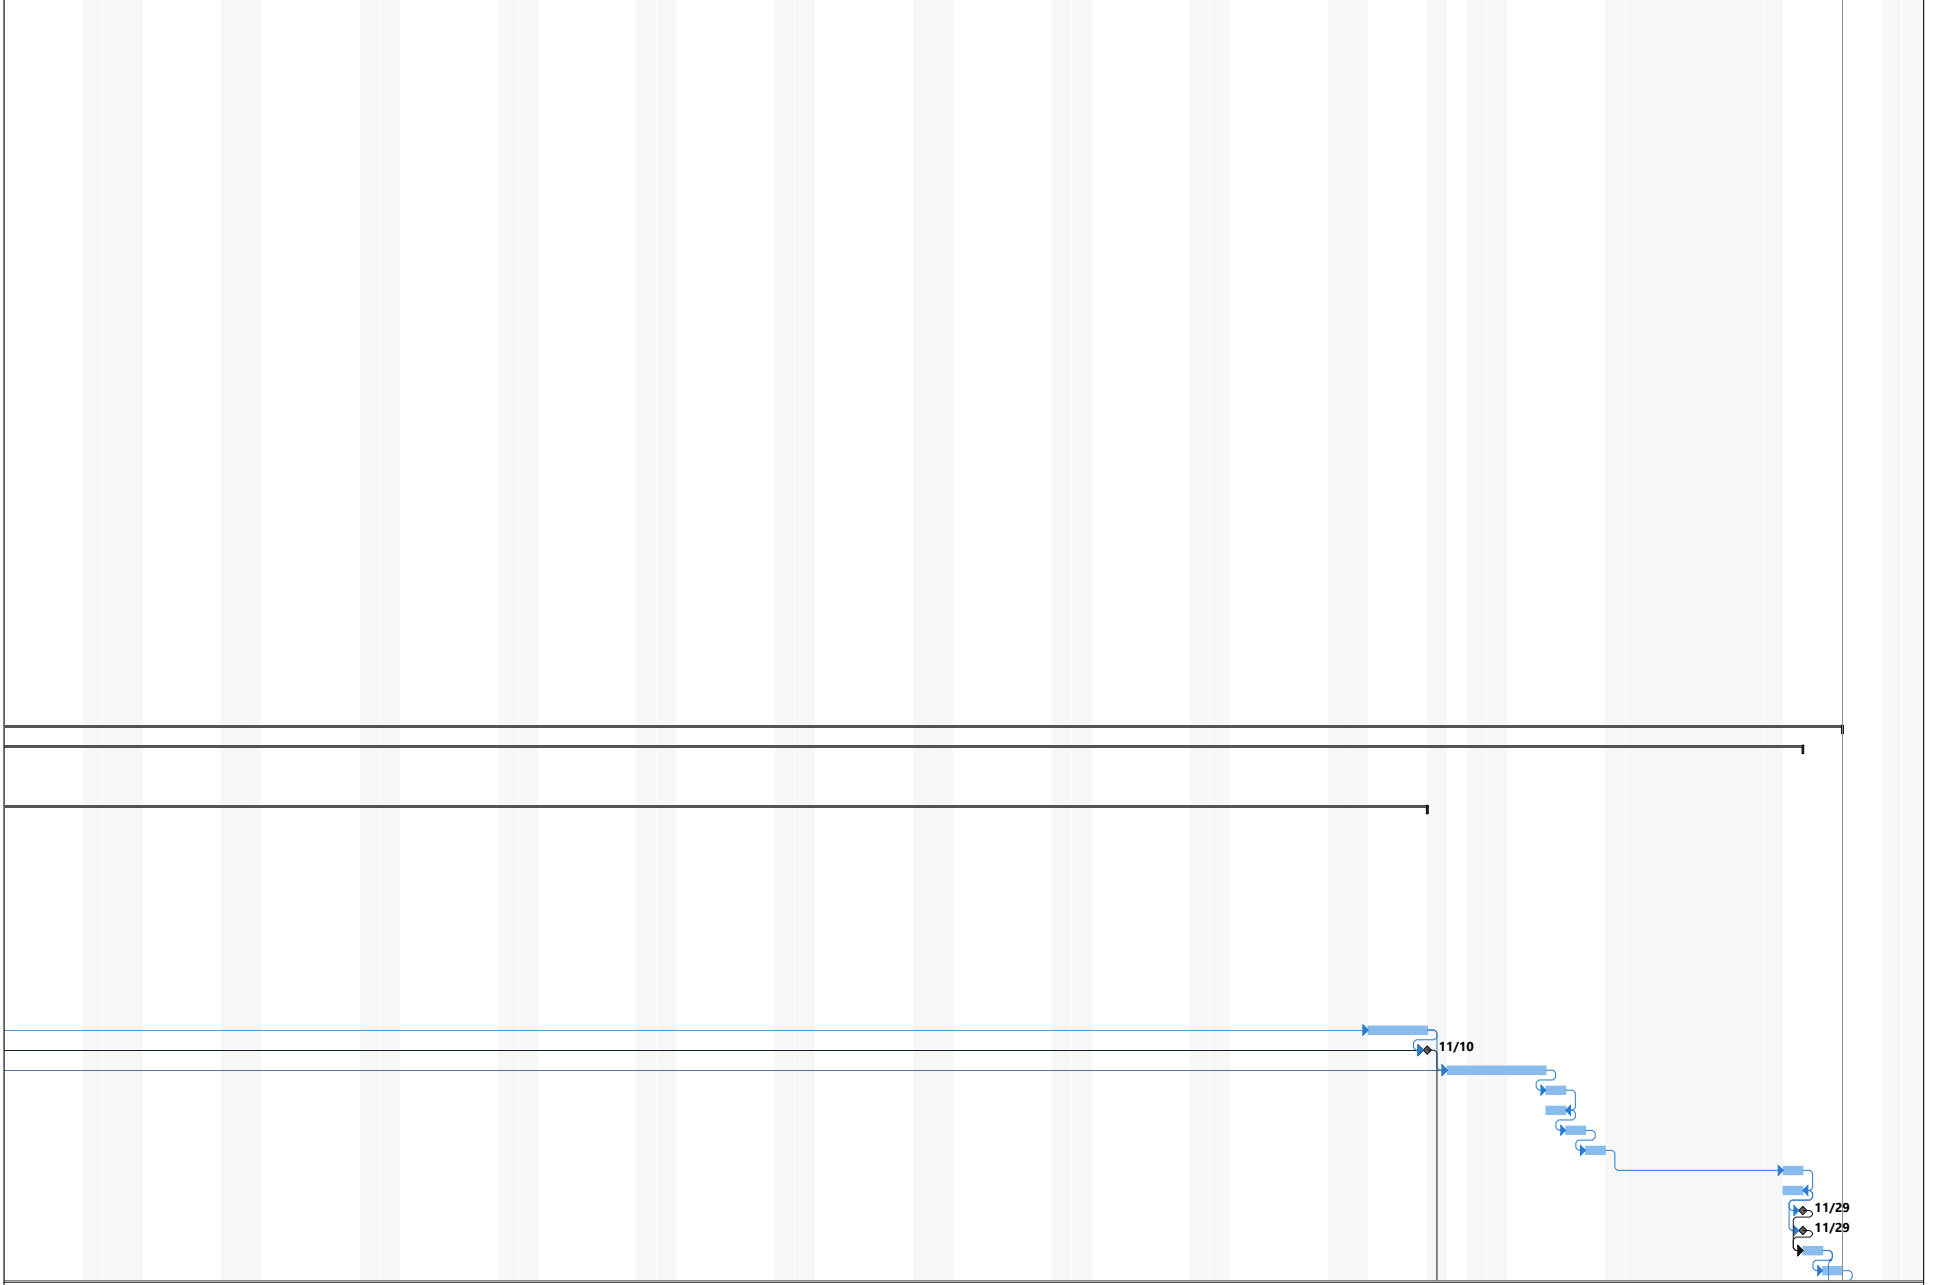



21	Sep 5, '21	Sep 12, '21	Sep 19, '21	Sep 26, '21	Oct 3, '21	Oct 10, '21	Oct 17, '21	Oct 24, '21	Oct 31, '21	Nov 7, '21	Nov 14, '21	Nov 21, '21	Nov 28, '21	Dec
T	S	S	S	S	S	S	S	S	S	S	S	S	S	S
W	M	M	M	M	M	M	M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F	F	F	F	F	F	F	F
S	S	S	S	S	S	S	S	S	S	S	S	S	S	S

12/1
12/1
